



Implementing Open Data Action Plan for the Kyrgyz Republic (P160933)

EUROPE AND CENTRAL ASIA | Kyrgyz Republic | Digital Development Global Practice |
 Recipient Executed Activities | Investment Project Financing | FY 2018 | Seq No: 1 | ARCHIVED on 05-Oct-2019 | ISR32098 |

Implementing Agencies: Ministry of Finance of the Kyrgyz Republic, State Committee on Information and Communication Technology

Key Dates

Key Project Dates

Bank Approval Date: 29-Aug-2017

Effectiveness Date: 05-Feb-2018

Original Closing Date: 10-Oct-2019

Revised Closing Date: 10-Oct-2019

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Development Objective is to enhance modern statistical and data management and sharing capabilities of the Recipient through the creation of an online data platform populated with open data sets, and to raise capacity among the public to access and use such data.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	<input type="checkbox"/> Satisfactory
Overall Implementation Progress (IP)	--	<input type="checkbox"/> Satisfactory

Implementation Status and Key Decisions

The key achievements are as follows:

- (i) During January 2019 and July 2019 missions, the SCITC PIU presented the overall results for the last period for the Open Data project, which were found to be moderately satisfactory.
- (ii) Based on inadequate delivery of the portal solution, it was decided by the Management of the SCITC to terminate the Contract with the portal vendor and entrust the State Enterprise "Infosystem" to develop the Open Data portal using CKAN platform in accordance with the ToR. Development of the portal is under control of the Chairman, the Deputy Chairman of the SCITC and the acting Project Director.
- (iii) Regarding the number of MoUs signed with public entities to supply Open Data, 18 MoUs have been signed. The project has already surpassed the end target (8 agencies). In 12 pilot government agencies, an analysis of state data disclosure for the open data portal was conducted. The pilot government agencies adopted internal open data action plans, and the open data sets have been identified to be placed on the Open Data portal. SCITC's Open Data Team have prepared an analytical note on the results of work with pilot government agencies. Based on this note, recommendations have been prepared for the Open Data Working Group and for the National Forum "Open Government." The World Bank task team recommended preparing the open datasets that should be based primarily on the results of a study on the demand side for



open data in Kyrgyzstan. It was also recommended that PIU should formulate visions for the development of innovative solutions based on open data, as well as the transition to Digital CASA - Kyrgyzstan project after the completion of this Open Data project (ex. transfer of open data to the G-Cloud).

(iv) SCITC's Open Data team with hired legal experts began a study to identify gaps regarding open data related legislation. During the study period, international best practices in the field of open data were reviewed. The results of this study were reflected on the abovementioned recommendations for the Open Data Working Group so that the Government of the Kyrgyz Republic can improve the legislation to create favorable conditions for the development of the Open Data Ecosystem in the country. SCITC's Open Data team have prepared two interim reports on the analysis of national and international legislation. The World Bank task team suggested holding a series of joint video conferences with the participation of leading international experts in the field of open data to share knowledge and experience. Open Data team visited Tashkent to share experience and learn from international experts attending Open Data events during the week of Sept 23-27.

(v) The Open Data team developed a communications strategy and a ToR for hiring a company to implement the strategy. The contract was signed in June 2019 with Qvazar, a local PR agency. The Bank team recommended aligning the open data communications strategy with that of Digital CASA - Kyrgyzstan project and other related communication activities to increase efficiency and optimize available resources. The World Bank task team placed special importance on strategic communications campaigns for the implementation of open data and recommended launching a press release when important datasets are disclosed.

The current closing date of the project is October 10, 2019. Extension of closing date until December 31, 2019 was requested to allow the use of the grant resources to complete some of the ongoing activities.

The following activities are planned to conduct before the end of the project:

- To develop and approve a standard instruction on the procedure for publishing open data by government agencies, as well as technical requirements to open data publication;
- To create the list of data sets of 12 pilot departments, to appoint responsible persons and publish in amount of not less than 700 data sets;
- To work out the composition of the data sets for compliance with preliminary technical requirement, as well as the composition of data provided;
- To organize testing of the portal and data sets, and work out testing results;
- To implement integration of the Open Data Portal with the sites/information systems of the ministries through API;
- To develop user guidelines and conduct training.

Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	--	☐Moderate

5. Results

Project Development Objective Indicators

☐Fully operational Open Data Portal (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	Yes	Yes
Date	01-Feb-2017	--	03-Oct-2019	10-Oct-2019

☐Number of data sets available on the Open Data Portal by end of project (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	--	116.00	200.00
Date	01-Feb-2017	--	03-Oct-2019	10-Oct-2019

□Number of MOUs signed with public entities to supply Open Data (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	12.00	8.00
Date	01-Feb-2017	--	28-Jun-2019	10-Oct-2019

Intermediate Results Indicators

□Number of capacity building events conducted (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	11.00	10.00
Date	01-Feb-2017	--	03-Oct-2019	10-Oct-2019

□Beneficiaries that feel project investments reflected their needs (percentage) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	80.00	90.00
Date	01-Feb-2017	--	03-Oct-2019	10-Oct-2019

□Total beneficiaries of training activities - female (number) (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	40.00	80.00

□Total beneficiaries of training activities - male (number) (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	30.00	120.00

□Beneficiaries that feel project inv. reflected their needs - male (number) (Number, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	108.00



□Project beneficiaries accessing Open Data (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	4,500.00	5,000.00
Date	01-Feb-2017	--	03-Oct-2019	10-Oct-2019

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P160933	TF-A5660	Effective	USD	0.45	0.45	0.00	0.40	0.05	89%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P160933	TF-A5660	Effective	11-Sep-2017	20-Oct-2017	05-Feb-2018	10-Oct-2019	10-Oct-2019

Cumulative Disbursements

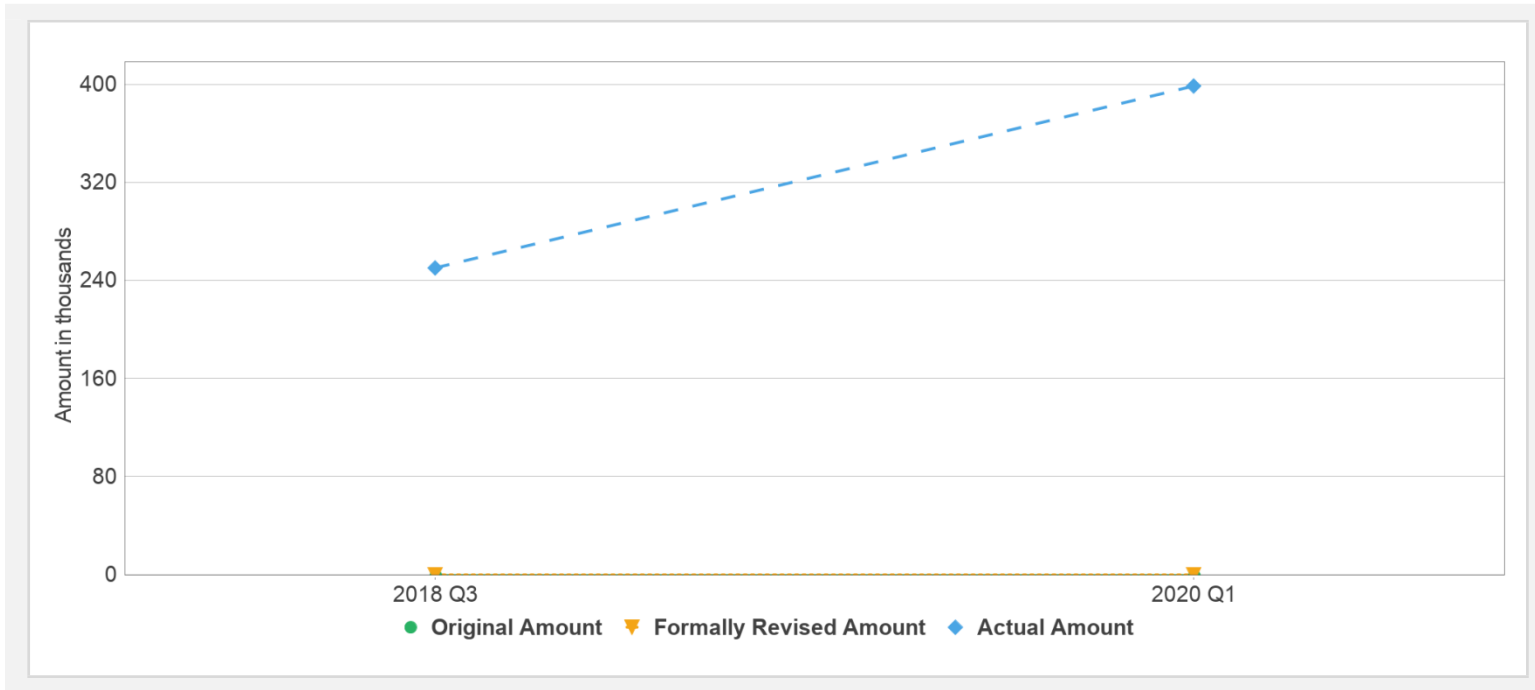

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
